🔴 RØD ALARM: KRITISK KOSTNADSSPREKK & LIKVIDITETSEKSPONERING (Per 31.10.2026)

Executive RAG Headline

1. DIAGNOSE (EVM): Prosjektet opererer med en kostnadseffektivitet på CPI 0.331 og et akkumulert kostnadsavvik på NOK -38.8M. Fysisk fremdrift meldes til SPI 1.156 som følge av forsert reaktormontasje.

Narrative Part1 Diagnose

2. DRIVER & LIKVIDITET: Bokførte kostnader (NOK 58.0M) og åpne leverandørforpliktelser (NOK 49.2M) gir en samlet finansiell eksponering på NOK 107.2M (536% av godkjent totalbudsjett).

Narrative Part2 Driver

3. REGNSKAPSMESSIG KONSEKVENS: Av de bokførte kostnadene er NOK 43.4M balanseført som anlegg under utførelse (AuC) etter IAS 38. Eksploderende sluttkostnad (EAC) utløser umiddelbart krav om nedskrivningstest etter IAS 36 før årsoppgjøret.

Narrative Part3 Accounting


4. PÅBUD TIL STYRET: 1) Umiddelbar innkjøpsfrys på alle nye rekvisisjoner. 2) Kanselleringsaudit av uleverte innkjøpsordrer (NOK 49,2M). 3) Innkall styret til ekstraordinært Stage-Gate møte for 30 dagers Technical Hold / Off-Ramp vurdering.

Narrative Part4 Action

20M	58M	19M	49M	107.20M
Budget at Completion (BAC)	Actual Cost (AC)	Earned Value (EV)	PO Open Commitment NOK	Total Financial Exposure

Cost Variance (CV)

by wbs_name

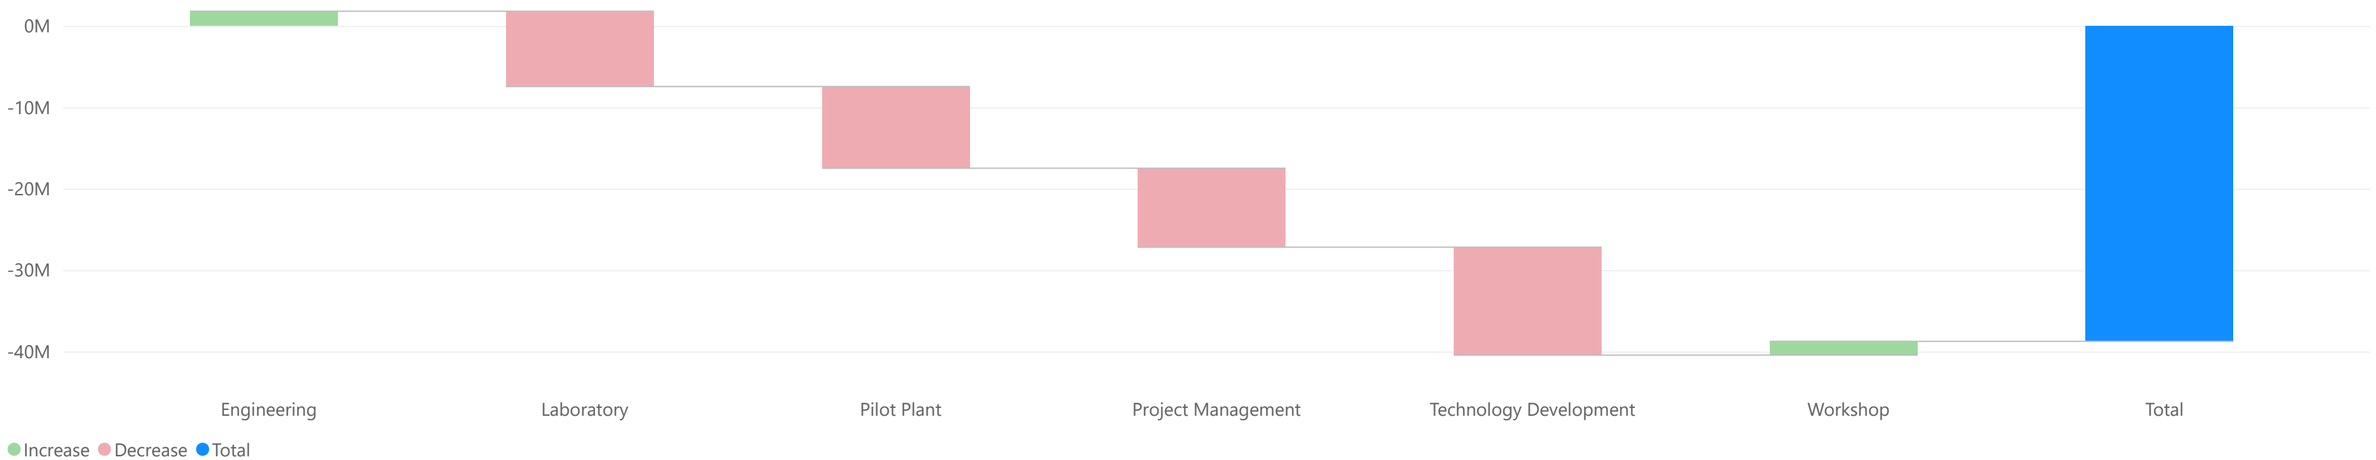


project_id

- [ ] (Blank)
- [ ] GP2026

20M	58M	19M	0.33	1.16	96.1%
Budget at Completion (BAC)	Actual Cost (AC)	Earned Value (EV)	Cost Performance Index (CPI)	Schedule Performance Inde...	Physical Progress % (Current)

Status Date Dynamic Line, Planned Value Cumulative (PV S-Curve), Actual Cost Cumulative (AC S-Curve) and Earned Value Cumulative (EV S-Curve)
by Period

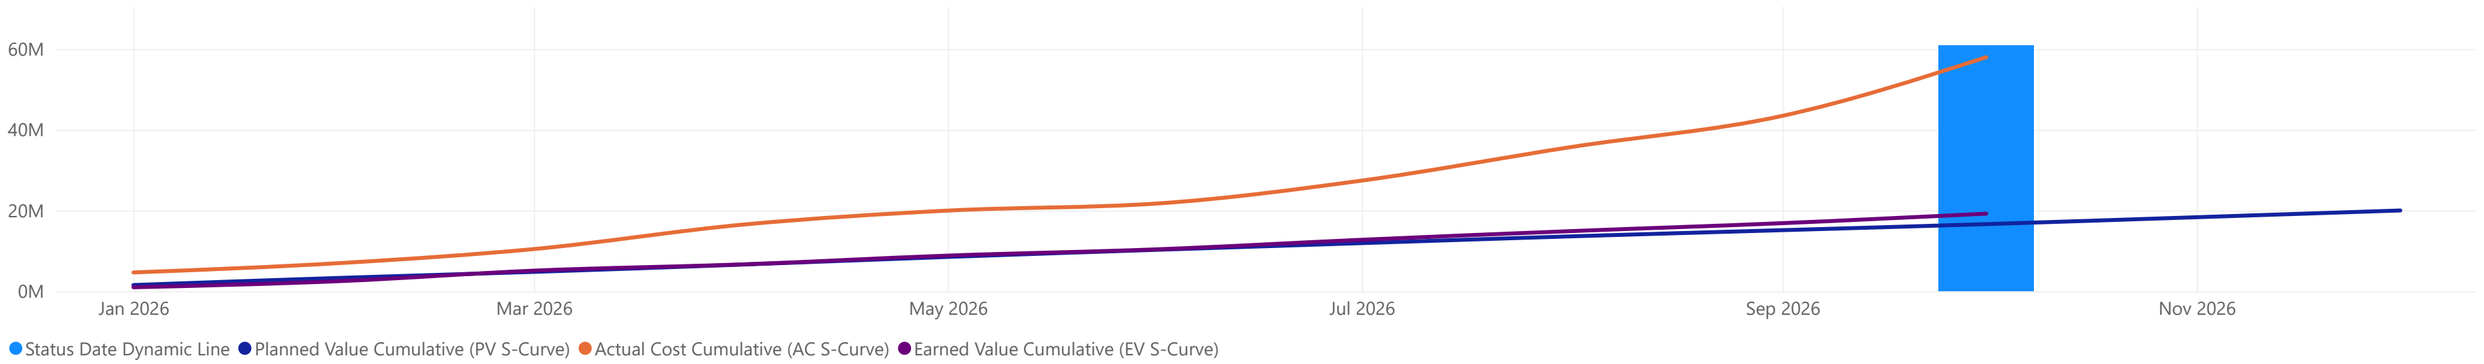

wbs_id	Budget at Completion (BAC)	Planned Value (PV)	Actual Cost (AC)	Budget Consumption Bar	Earned Value (EV)	Cost Variance (CV)	Cost Variance Bar	Cost Performance Index (CPI)	CPI Status RAG	Schedule Performance Index (SPI)	SPI Status RAG	Physical Progress Bar
WBS-100	**3,581,799**	**3,002,371**	**1,630,813**	**45.5%**	**3,441,336**	**1,810,523**	**(+1.8M)**	**2.11**	**Green (2.11)**	**1.15**	**Green (1.15)**	**97.1%**
Engineering	3,581,799	3,002,371	1,630,813	45.5%	3,441,336	1,810,523	(+1.8M)	2.11	Green (2.11)	1.15	Green (1.15)	97.1%
WBS-200	**3,323,265**	**2,834,129**	**12,446,210**	**374.5%**	**3,192,941**	**-9,253,270**	**(-9.3M)**	**0.26**	**Red (0.26)**	**1.13**	**Green (1.13)**	**97.1%**
Laboratory	3,323,265	2,834,129	12,446,210	374.5%	3,192,941	-9,253,270	(-9.3M)	0.26	Red (0.26)	1.13	Green (1.13)	97.1%
WBS-300	**3,359,641**	**2,771,120**	**13,263,844**	**394.8%**	**3,227,891**	**-10,035,954**	**(-10.0M)**	**0.24**	**Red (0.24)**	**1.16**	**Green (1.16)**	**97.1%**
Pilot Plant	3,359,641	2,771,120	13,263,844	394.8%	3,227,891	-10,035,954	(-10.0M)	0.24	Red (0.24)	1.16	Green (1.16)	97.1%
WBS-400	**3,195,297**	**2,681,477**	**1,379,679**	**43.2%**	**3,069,991**	**1,690,312**	**(+1.7M)**	**2.23**	**Green (2.23)**	**1.14**	**Green (1.14)**	**97.1%**
Workshop	3,195,297	2,681,477	1,379,679	43.2%	3,069,991	1,690,312	(+1.7M)	2.23	Green (2.23)	1.14	Green (1.14)	97.1%
WBS-500	**3,150,476**	**2,508,688**	**16,285,294**	**516.9%**	**3,026,928**	**-13,258,367**	**(-13.3M)**	**0.19**	**Red (0.19)**	**1.21**	**Green (1.21)**	**94.1%**
Technology Development	3,150,476	2,508,688	16,285,294	516.9%	3,026,928	-13,258,367	(-13.3M)	0.19	Red (0.19)	1.21	Green (1.21)	94.1%
WBS-600	**3,389,522**	**2,823,086**	**12,962,199**	**382.4%**	**3,256,600**	**-9,705,599**	**(-9.7M)**	**0.25**	**Red (0.25)**	**1.15**	**Green (1.15)**	**94.1%**
Project Management	3,389,522	2,823,086	12,962,199	382.4%	3,256,600	-9,705,599	(-9.7M)	0.25	Red (0.25)	1.15	Green (1.15)	94.1%
Total	**20,000,000**	**16,620,871**	**57,968,041**	**289.8%**	**19,215,686**	**-38,752,355**	**(-38.8M)**	**0.33**	**Red (0.33)**	**1.16**	**Green (1.16)**	**96.1%**

Overall Project Health RAG


🔴 CRITICAL OVERRUN (CPI: 0.33 | Open PO: 49.2M NOK)


Root Cause Primary Diagnosis


FAST-TRACKING / PREMATURE FORCING: Schedule is 5 weeks ahead (SPI 1.16), but achieved via excessive premium freight, unbudgeted equipment purchases, and heavy overtime. Work delivered at 3x planned unit cost.

Root Cause Driver Decomposition

VARIANCE DRIVERS (Total CV: --38.75M NOK):
1. Technology Development (WBS-500): -13.13M NOK (Overrun +417%)
2. Equipment & Machinery (CE400): -10.15M NOK (Overrun +312%)
3. Pilot Plant Assembly (WBS-300): -9.90M NOK (Overrun +295%)
4. Internal Labor / Overtime (CE100): -9.52M NOK (Overrun +263%)...

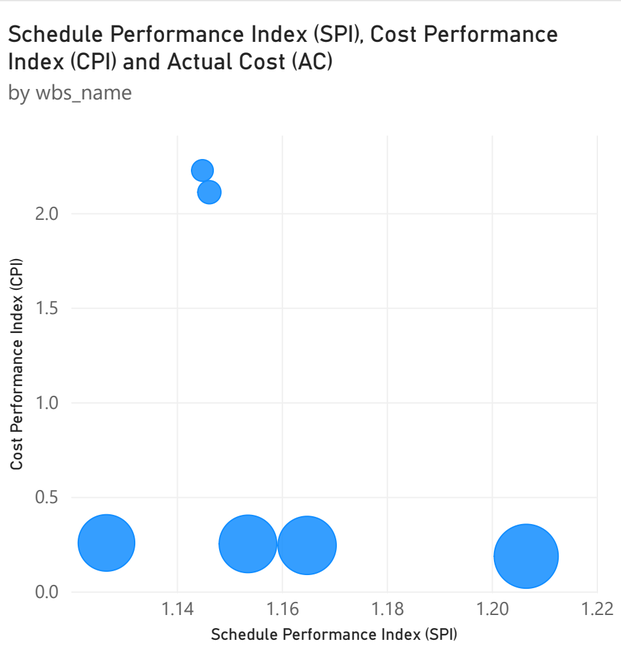

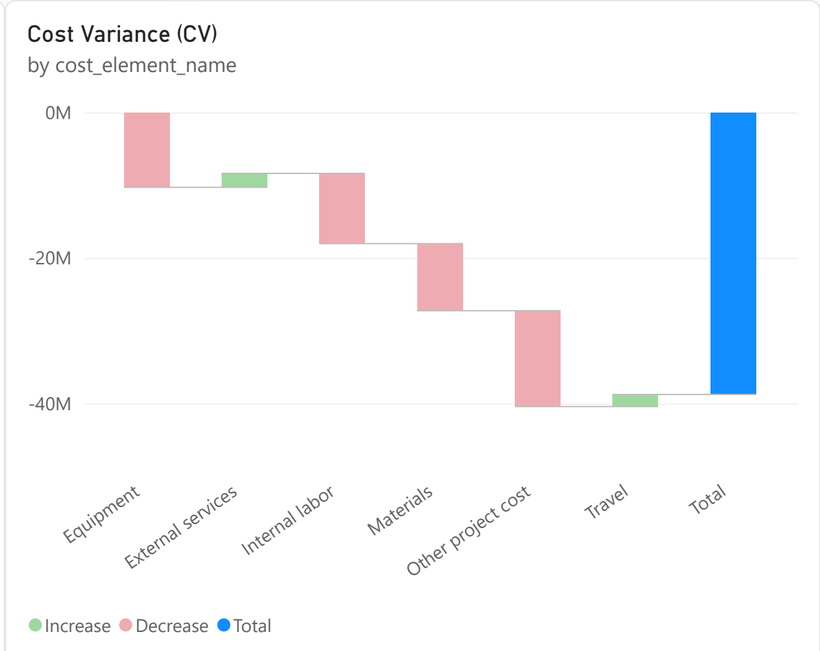

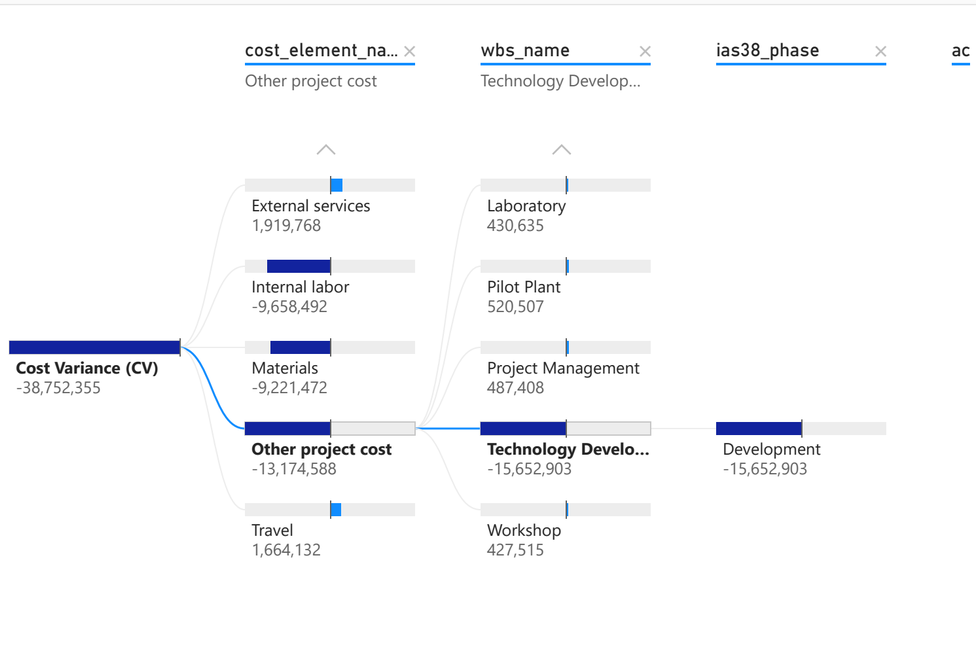

106M
PO Amount NOK


57M
PO Invoiced NOK

49M
PO Open Commitment NOK

46.4%
PO Open Commitment %


vendor_name	currency	PO Amount NOK	PO Invoiced NOK	PO Open Commitment NOK	PO Commitment Exposure Bar	PO Commitment Exposure RAG	po_status
Synthetic Vendor 01	EUR	1,321,918	1,252,012	69,906	■□□□□□□□□ 5.3%	Controlled Exposure (0.07M)	Partially Invoiced
Synthetic Vendor 01	NOK	104,334	0	104,334	■■■■■■■■■ 100.0%	High Exposure (0.10M)	Open Uninvoiced
Synthetic Vendor 01	NOK	69,399	29,052	40,348	■■■■■□□□□ 58.1%	Moderate Exposure (0.04M)	Partially Invoiced
Synthetic Vendor 01	USD	1,313,657	0	1,313,657	■■■■■■■■■ 100.0%	High Exposure (1.31M)	Open Uninvoiced
Synthetic Vendor 01	USD	2,808,567	2,229,266	579,301	■■□□□□□□□ 20.6%	Moderate Exposure (0.58M)	Partially Invoiced
Synthetic Vendor 02	EUR	1,417,938	0	1,417,938	■■■■■■■■■ 100.0%	High Exposure (1.42M)	Open Uninvoiced
Synthetic Vendor 02	EUR	1,667,146	1,069,439	597,707	■■■■□□□□□ 35.9%	Moderate Exposure (0.60M)	Partially Invoiced
Synthetic Vendor 02	NOK	176,681	0	176,681	■■■■■■■■■ 100.0%	High Exposure (0.18M)	Open Uninvoiced
Synthetic Vendor 02	NOK	248,122	168,198	79,925	■■■□□□□□□ 32.2%	Controlled Exposure (0.08M)	Partially Invoiced
Synthetic Vendor 02	USD	2,939,887	1,930,699	1,009,188	■■■□□□□□□ 34.3%	Moderate Exposure (1.01M)	Partially Invoiced
Synthetic Vendor 03	EUR	1,770,679	0	1,770,679	■■■■■■■■■ 100.0%	High Exposure (1.77M)	Open Uninvoiced
Synthetic Vendor 03	EUR	2,009,872	1,345,239	664,633	■■■□□□□□□ 33.1%	Moderate Exposure (0.66M)	Partially Invoiced
Synthetic Vendor 03	NOK	173,903	177,389	0	□□□□□□□□□ 0.0%	Controlled Exposure (0.00M)	Fully Invoiced
Synthetic Vendor 03	NOK	51,735	29,276	22,459	■■■■□□□□□ 43.4%	Moderate Exposure (0.02M)	Partially Invoiced
Synthetic Vendor 03	USD	299,134	0	299,134	■■■■■■■■■ 100.0%	High Exposure (0.30M)	Open Uninvoiced
Synthetic Vendor 03	USD	1,558,026	1,430,226	127,799	■□□□□□□□□ 8.2%	Controlled Exposure (0.13M)	Partially Invoiced
Synthetic Vendor 04	EUR	549,997	372,979	177,018	■■■□□□□□□ 32.2%	Controlled Exposure (0.18M)	Partially Invoiced
Synthetic Vendor 04	NOK	89,799	90,866	0	□□□□□□□□□ 0.0%	Controlled Exposure (0.00M)	Fully Invoiced
Synthetic Vendor 04	NOK	52,403	0	52,403	■■■■■■■■■ 100.0%	High Exposure (0.05M)	Open Uninvoiced
Synthetic Vendor 04	NOK	37,107	25,089	12,018	■■■□□□□□□ 32.4%	Controlled Exposure (0.01M)	Partially Invoiced
Synthetic Vendor 04	USD	1,154,261	0	1,154,261	■■■■■■■■■ 100.0%	High Exposure (1.15M)	Open Uninvoiced
Synthetic Vendor 04	USD	1,544,167	1,178,821	365,346	■■□□□□□□□ 23.7%	Controlled Exposure (0.37M)	Partially Invoiced
Synthetic Vendor 05	EUR	146,196	0	146,196	■■■■■■■■■ 100.0%	High Exposure (0.15M)	Open Uninvoiced
Synthetic Vendor 05	EUR	2,201,972	1,854,988	346,984	■■□□□□□□□ 15.8%	Controlled Exposure (0.35M)	Partially Invoiced
Synthetic Vendor 05	NOK	60,639	0	60,639	■■■■■■■■■ 100.0%	High Exposure (0.06M)	Open Uninvoiced
Synthetic Vendor 05	NOK	190,524	128,102	62,422	■■■□□□□□□ 32.8%	Controlled Exposure (0.06M)	Partially Invoiced
Synthetic Vendor 05	USD	1,910,542	1,807,825	102,717	■□□□□□□□□ 5.4%	Controlled Exposure (0.10M)	Partially Invoiced
Synthetic Vendor 06	EUR	782,811	0	782,811	■■■■■■■■■ 100.0%	High Exposure (0.78M)	Open Uninvoiced
Synthetic Vendor 06	EUR	2,250,703	1,232,405	1,018,298	■■■■■□□□□ 45.2%	Moderate Exposure (1.02M)	Partially Invoiced
Total		**106,173,112**	**56,946,401**	**49,233,752**	■■■■■□□□□ **46.4%**	**High Exposure (>25M)**	

PO Amount NOK
by currency

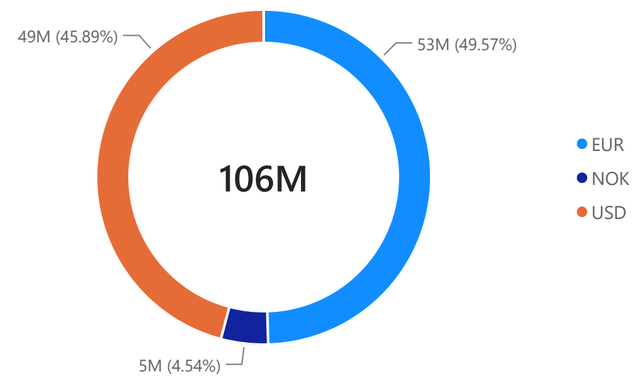

58M	43M	15M	74.8%
Actual Cost (AC)	Actual Cost Capitalized (AuC)	Actual Cost Expensed (P&L)	Capitalization Rate %

Actual Cost (AC)
by accounting_bucket

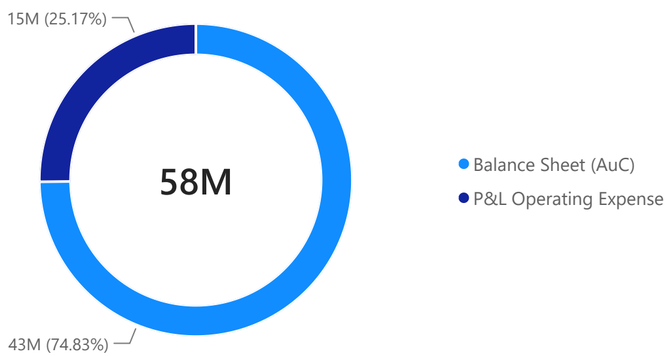

wbs_id	Actual Cost (AC)	Actual Cost Capitalized (AuC)	Actual Cost Expensed (P&L)	Capitalization Rate %	AuC Capitalization Bar	AuC Capitalization Ra
WBS-100	**1,630,813**		**1,630,813**			
Engineering	**1,630,813**		**1,630,813**			
Research	1,630,813		1,630,813			
WBS-200	**12,446,210**	**12,446,210**		**100.0%**	**100.0%**	**High Impairment**
Laboratory	**12,446,210**	**12,446,210**		**100.0%**	**100.0%**	**High Impairment**
Development	12,446,210	12,446,210		100.0%	100.0%	High Impairment
WBS-300	**13,263,844**	**13,263,844**		**100.0%**	**100.0%**	**High Impairment**
Pilot Plant	**13,263,844**	**13,263,844**		**100.0%**	**100.0%**	**High Impairment**
Development	13,263,844	13,263,844		100.0%	100.0%	High Impairment
WBS-400	**1,379,679**	**1,379,679**		**100.0%**	**100.0%**	**High Impairment**
Workshop	**1,379,679**	**1,379,679**		**100.0%**	**100.0%**	**High Impairment**
Development	1,379,679	1,379,679		100.0%	100.0%	High Impairment
WBS-500	**16,285,294**	**16,285,294**		**100.0%**	**100.0%**	**High Impairment**
Technology Development	**16,285,294**	**16,285,294**		**100.0%**	**100.0%**	**High Impairment**
Development	16,285,294	16,285,294		100.0%	100.0%	High Impairment
WBS-600	**12,962,199**		**12,962,199**			
Total	**57,968,041**	**43,375,028**	**14,593,013**	**74.8%**	**74.8%**	**Elevated AuC (60**

CRITICAL IMPAIRMENT WARNING (IAS 36): AuC Capitalization has reached 43.38M NOK (74.8% of total expenditure). Since budget overrun is +190% (CPI 0.33), immediate impairment test is required against future discounted cash flows.

IAS 36 Impairment Callout

change_order_id	wbs_id	status	Change Order Status RAG	requested_amount_nok	approved_amount_nok	Change Order Exposure Bar
CO001	WBS-200	APPROVED	Approved	323,528.00	217,871.00	324k
CO002	WBS-300	REJECTED	Rejected	212,832.00		213k
CO003	WBS-400	IMPLEMENTED	Implemented	32,575.00	206,762.00	33k
CO004	WBS-500	SUBMITTED	Pending Approval	227,556.00		228k
CO005	WBS-600	APPROVED	Approved	208,875.00	151,642.00	209k
CO006	WBS-100	REJECTED	Rejected	276,555.00		277k
CO007	WBS-200	IMPLEMENTED	Implemented	30,253.00	208,832.00	30k
CO008	WBS-300	SUBMITTED	Pending Approval	241,717.00		242k
CO009	WBS-400	APPROVED	Approved	269,306.00	43,079.00	269k
CO010	WBS-500	REJECTED	Rejected	341,245.00		341k
CO011	WBS-600	IMPLEMENTED	Implemented	37,131.00	174,120.00	37k
CO012	WBS-100	SUBMITTED	Pending Approval	308,312.00		308k
CO013	WBS-200	APPROVED	Approved	310,576.00	48,661.00	311k
CO014	WBS-300	REJECTED	Rejected	85,899.00		86k
CO015	WBS-400	IMPLEMENTED	Implemented	198,465.00	246,364.00	198k
CO016	WBS-500	SUBMITTED	Pending Approval	162,167.00		162k
CO017	WBS-600	APPROVED	Approved	226,290.00	177,303.00	226k
CO018	WBS-100	REJECTED	Rejected	159,933.00		160k
Total			**Total (18 COs)**			**3,653k**

activity_id	activity_name	wbs_id	status	Activity Status RAG	Activity Progress Bar	progress_pct	planned_finish
A001	GreenPilot activity 001	WBS-100	Completed	Completed (100%)	100%	100	Saturday, January 10, 2026
A002	GreenPilot activity 002	WBS-200	Completed	Completed (100%)	100%	100	Monday, January 19, 2026
A003	GreenPilot activity 003	WBS-300	Completed	Completed (100%)	100%	100	Thursday, January 22, 2026
A004	GreenPilot activity 004	WBS-400	Completed	Completed (100%)	100%	100	Tuesday, January 20, 2026
A005	GreenPilot activity 005	WBS-500	Completed	Completed (100%)	100%	100	Saturday, January 24, 2026
A006	GreenPilot activity 006	WBS-600	Completed	Completed (100%)	100%	100	Sunday, February 01, 2026
A007	GreenPilot activity 007	WBS-100	Completed	Completed (100%)	100%	100	Monday, February 02, 2026
A008	GreenPilot activity 008	WBS-200	Completed	Completed (100%)	100%	100	Sunday, February 01, 2026
A009	GreenPilot activity 009	WBS-300	Completed	Completed (100%)	100%	100	Saturday, February 14, 2026
A010	GreenPilot activity 010	WBS-400	Completed	Completed (100%)	100%	100	Wednesday, February 25, 2026
A011	GreenPilot activity 011	WBS-500	Completed	Completed (100%)	100%	100	Thursday, February 26, 2026
A012	GreenPilot activity 012	WBS-600	Completed	Completed (100%)	100%	100	Thursday, February 26, 2026
A013	GreenPilot activity 013	WBS-100	Completed	Completed (100%)	100%	100	Wednesday, February 18, 2026
Total				**Avg (96.1%)**	**96%**		

Prescriptive Controller Actions


MANDATORY CONTROLLER ACTIONS (ELKEM PILOT CONTROL):

1. [IMMEDIATE PO FREEZE] Cancel unfulfilled line items in Fact_PurchaseOrders. Open exposure is currently 49.23M NOK across foreign vendors.
2. [IFRS / IAS 36 IMPAIRMENT REVIEW] Capitalized AuC on balance sheet has reached 43.38M NOK. Corporate finance must assess if future commercial cash flows support this asset base.
3. [CHANGE ORDER BASELINE RESET] 14 out of 18 Change Orders remain unapproved or pending. The steering committee must establish an Over-Target Baseline (OTB) of 62.5M NOK.
4. [TIME CONTROL] 96.08% physical completion reached. Close remaining 4 active activities (A097-A100) and demobilize external personnel.

48M	3M	-45M	49M
Total Cash Outflow NOK	Enova Grant Cash In NOK	Cumulative Net Cash Flow NOK	PO Open Commitment NOK

Supplier AP Paid NOK, Internal Payroll Paid NOK, Enova Grant Cash In NOK and Cumulative Net Cash Flow NOK

by Period

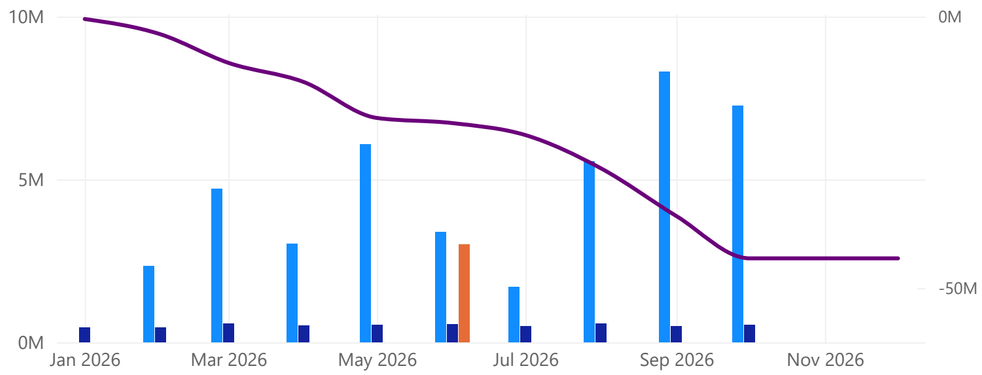

department	Koststed Kode (Fiskå)	Faktiske Timer Koststed	Personalkostnad Koststed NOK	Andel Timer Koststed %	Koststed Timer Bar
Finance	**CC-4300**	**3,394.0**	**1,798,820**	**34.7%**	**34.7%**
Controller	CC-4300	747.5	396,175	7.6%	7.6%
Engineer	CC-4300	743.0	393,790	7.6%	7.6%
Project Manager	CC-4300	378.0	200,340	3.9%	3.9%
Scientist	CC-4300	765.0	405,450	7.8%	7.8%
Technician	CC-4300	760.5	403,065	7.8%	7.8%
Operations	**CC-4100**	**3,379.5**	**1,791,135**	**34.6%**	**34.6%**
Controller	CC-4100	373.5	197,955	3.8%	3.8%
Engineer	CC-4100	765.5	405,715	7.8%	7.8%
Project Manager	CC-4100	747.0	395,910	7.6%	7.6%
Scientist	CC-4100	746.0	395,380	7.6%	7.6%
Technician	CC-4100	747.5	396,175	7.6%	7.6%
Total	**CC-4100..4300**	**9,772.5**	**5,179,425**	**100.0%**	**100.0%**

Period	Early Warning Status RAG	Early Warning PO Exposure Bar	Planned Value (PV)	Actual Cost (AC)	Cost Performance Index (CPI)	Schedule Performance Index (SPI)	Early Warning Controller Action
1/1/2026	YELLOW: Burn-rate > 1.5x — WARNING	50.4% BAC	1,534,314	4,653,705	0.21	0.64	Avstemming av åpne PO-er og de-scoping av lab-tester.
2/1/2026	YELLOW: Burn-rate > 1.5x — WARNING	76.7% BAC	3,336,906	2,376,228	0.36	0.76	Avstemming av åpne PO-er og de-scoping av lab-tester.
3/1/2026	RED: PO > 100% BAC — CRITICAL	148.9% BAC	4,791,322	3,413,810	0.49	1.06	Krav om Stage-Gate Freeze og formell styrebehandlet OTB.
4/1/2026	RED: PO > 100% BAC — CRITICAL	175.5% BAC	6,617,298	6,087,616	0.40	1.01	Krav om Stage-Gate Freeze og formell styrebehandlet OTB.
5/1/2026	RED: PO > 100% BAC — CRITICAL	204.9% BAC	8,495,891	3,443,782	0.44	1.04	Krav om Stage-Gate Freeze og formell styrebehandlet OTB.
6/1/2026	RED: PO > 100% BAC — CRITICAL	266.3% BAC	10,269,252	1,770,061	0.48	1.01	Krav om Stage-Gate Freeze og formell styrebehandlet OTB.
7/1/2026	RED: PO > 100% BAC — CRITICAL	330.0% BAC	11,914,645	5,659,320	0.47	1.07	Krav om Stage-Gate Freeze og formell styrebehandlet OTB.
8/1/2026	RED: PO > 100% BAC — CRITICAL	367.3% BAC	13,604,859	8,349,815	0.42	1.10	Krav om Stage-Gate Freeze og formell styrebehandlet OTB.
9/1/2026	RED: PO > 100% BAC — CRITICAL	459.3% BAC	15,126,181	7,696,088	0.39	1.11	Krav om Stage-Gate Freeze og formell styrebehandlet OTB.
10/1/2026	RED: PO > 100% BAC — CRITICAL	530.9% BAC	16,620,871	14,517,615	0.33	1.16	Krav om Stage-Gate Freeze og formell styrebehandlet OTB.
11/1/2026			18,332,521				
12/1/2026			20,000,000				
Total	**RED: PO > 100% BAC — CRITICAL**	**530.9% BAC**	**16,620,871**	**57,968,041**	**0.33**	**1.16**	**Krav om Stage-Gate Freeze og formell styrebehandlet OTB.**

AI INSIGHTS & ROTÅRSAKSANALYSE: Nedbrytingstreet og variansmotoren identifiserer WBS 1.3 (Pilot Furnace Construction & Procurement) og valutabundne utstyrsleveranser som de dominerende driverne for kostnadssprekk og rød status.

Page05_AI_Insights_Narrative

